Benton County Riparian and Wetland Project—Project Timeline

Tasks	Start	Finish
1.1 Convene and Coordinate Stakeholder and Technical Advisory Groups	7/30/2009	6/30/2011
Staff contact and Finalization of Advisory Group members	7/30/2009	9/30/2009
Plan and conduct Advisory Group 'kickoff meeting	9/30/2009	11/13/2009
Bi-monthly meetings and communication	9/30/2009	6/30/2011
1.2 Develop and maintain Project web page and e-mail list	7/30/2009	6/30/2011
2.1 Riparian and Wetlands Program Options Analysis consistent with Oregon Administrative Rules	7/30/2009	12/15/2009
Prepare supporting materials	8/3/2009	12/15/2009
Advisory Groups review and support specific Program Option	10/1/2009	12/30/2009
2.2 Program Option Presentation to Board of Commissioners	1/12/2010	1/12/2010
Option approved by Board	1/12/2010	1/29/2010
3.1 Pilot comparative analysis of processed LIDAR data to current riparian and wetland maps	7/30/2009	6/30/2010
Gain LIDAR coverage; determine feasible uses	8/31/2009	12/1/2009
Complete analysis and draft short report of feasible uses during project	10/1/2009	12/15/2009

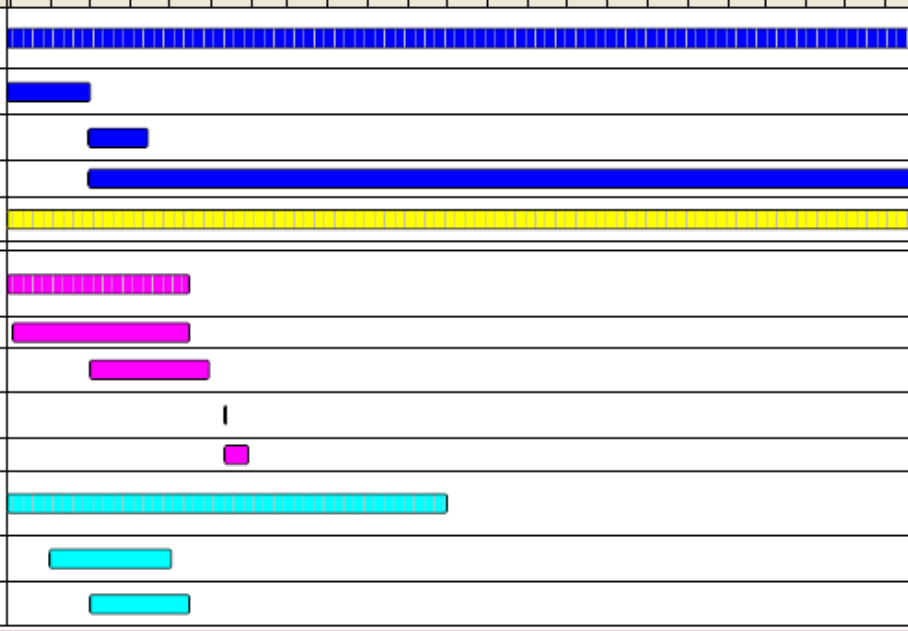

Task Name	Start	Finish
3.2 GIS mapping of riparian corridors and wetlands	10/1/2009	6/30/2010
Existing GIS base data layers compiled into single Arc Map project	10/1/2009	10/30/2009
Produce Enforced Drainage stream channel GIS layer from LIDAR acquired data	10/30/2009	3/30/2010
Review and input from Advisory Groups	4/1/2010	6/30/2010
3.3 Select ground-truth field assessments of riparian corridor and wetlands; determine GIS analysis accuracy	7/1/2010	9/1/2010
Determine suitable field assessment locations based on Advisory group and staff input	7/1/2010	7/30/2010
Completion of ground-truthing (GPS)	8/2/2010	10/1/2010
Compare ground truth data with GIS/LIDAR mapping to determine accuracy and future work needs	10/1/2010	12/1/2010
4.1 Provide Inventory and Program Options Analysis and other project work to residents through countywide Community Meetings	7/1/2010	12/30/2010
Planning and completion of five Countywide Community Meetings	7/1/2010	11/30/2010
Stakeholder input captured and presented to Advisory Group and staff; inform final program requirements/ incentives	11/1/2010	2/1/2011
4.2 Project Updates and Outreach to Stakeholders (website, mailing lists, phone)	7/30/2009	6/30/2011

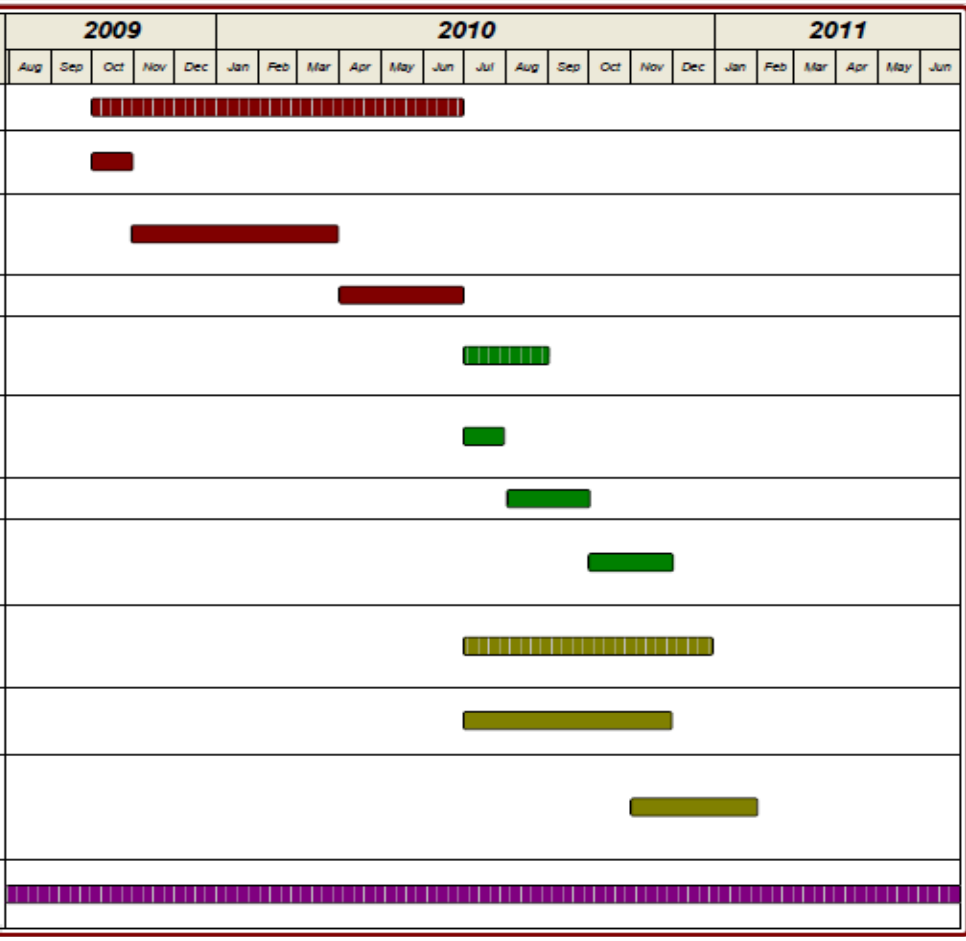

TURN OVER
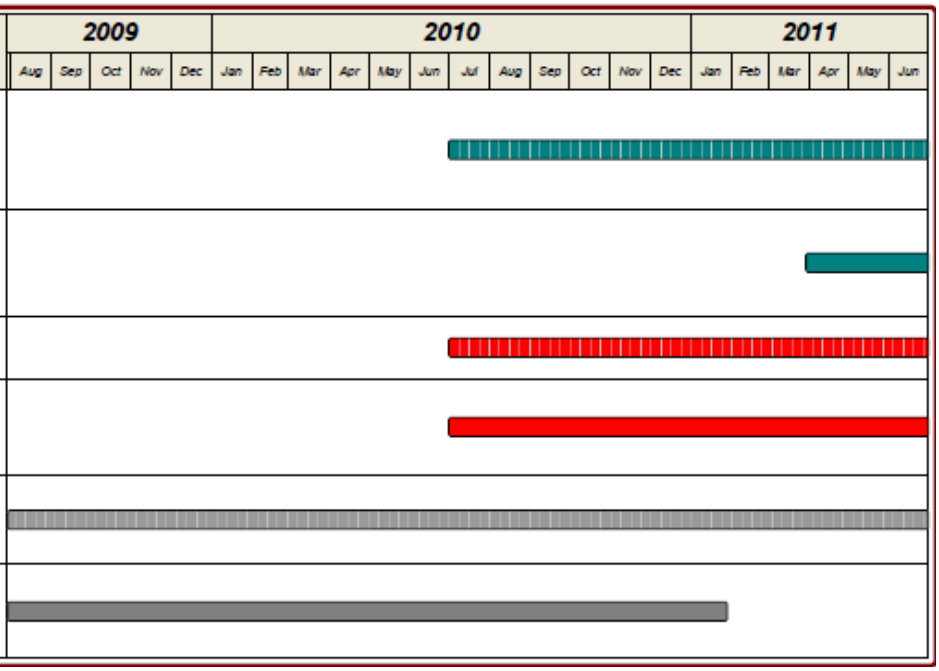
Task Name	Start	Finish
5.1 Inventory data (riparian corridor and wetlands) used to analyze the impacts of protecting resources and develop a recommend protection program	7/1/2010	6/30/2011
Gather Advisory Groups, County Commissioners and stakeholder input to amend and finalize protection program	3/30/2011	6/30/2011
5.2 Draft final land use regulations for adoption into the Benton County Development Code	7/1/2010	6/30/2011
'Hearings ready' ordinance prepared and presented for Board of Commissioners formal review and adoption	7/1/2010	6/30/2011
5.3 Develop incentives for riparian corridor and wetland protection and restoration within protection/ planning areas	7/30/2009	6/30/2011
Determine Local, State, Federal incentives available to Program affected organizations and residents	7/30/2009	1/28/2011
